


Station Information Report

Solar and Meteorological Station

World Bank – Shinyanga, Tanzania



Revision	Date	Author	Checked	Approved	Comments
Rev 0	08 April 2020	M.D. Johnstone	J. van Jaarsveldt	M. de Jager	First Issue
Rev 1					
Rev 2					





Solar & Meteorological Station – Installation Report

Contents

1	Introduction	4
2	Station Summary	6
3	Map of area	7
4	Site layout	8
5	Instrument list, serial numbers and multipliers	. 10
6	Supporting hardware and communication peripherals	. 11
7	Data logger wiring	. 12
8	Power circuit diagram	. 14
9	Detail Photographs	. 15
10	Terrain Photographs	. 22
11	Station Photographs	. 29
12	Calibration Certificates	. 36



1 Introduction

NOTE: This project occurred during the COVID19 pandemic outbreak. Any impact on the data quality as a result of the pandemic will be recorded in the monthly quality feedback report alongside other noteworthy events for the affected month.

The World Bank initiated a project with funding from the Energy Sector Management Assistance Program (ESMAP) to, amongst others, support the East African Power Pool (EAPP) in doing renewable energy resource assessments. The focus for this particular section of the project is to get high quality bankable irradiance measurements, high quality supporting meteorological measurements and to promote the awareness of the resource potential of solar energy.

The project is orientated around sites considered for large-scale solar power plant development in the near future. The on-site measured data generated from this project for the applicable term is to be used in conjunction with overlapping and historic satellite derived data for the same location in order to generate a bankable data set, subsequently providing enhanced data accuracy for locations where there may be substantial project investments. The data complements the global resource data available for free via the Global Solar Atlas (https://globalsolaratlas.info).

GeoSUN Africa has been awarded the contract to execute the on-site measurement related aspects of the project. The assignment for GeoSUN Africa is the following:

- An inception mission which involves visiting the proposed site locations and selecting
 the optimal location for the measurement equipment. The outcome of this inception
 mission is this implementation plan where sites and stations tiers are proposed;
- Providing high quality measuring equipment for each site, in line with the technical specifications;
- Installation of measurement equipment as well as subsequent Site Installation Report and photographs for each site;
- Hosting and providing two years of high quality, 'bankable' meteorological data relevant for solar resource assessment and project development, including upload to an 'open data' platform for public dissemination;
- Ensuring maintenance, security, local cleaning/caretaking, and mitigation against extreme weather events and corrosion;
- Ensuring strong local involvement and capacity building at all stages of the measurement campaign;
- Decommissioning of all sites at the end of the measurement campaign, unless separate arrangements are made with one or more host institutions to continue with measurements outside of this assignment/contract.

This document acts as the Site Installation Report which follows the commissioning of the site, outlining the site location, site characteristics, technical specifications, calibration procedures, and all other relevant information to allow data users to fully understand the site and ensure the bankability of the measurement data. The Site Installation Report is contains photographs of the site and the surrounding terrain.

The measurement data from the site will be continuously transferred to GeoSUN's central data repository, and shall then be transferred to the World Bank on a monthly basis in both raw and



Solar & Meteorological Station – Installation Report

quality controlled formats according to the specifications developed by ESMAP. This data will be delivered via an online file sharing platform one month in arears. Site Measurement Reports will accompany the delivery of monthly data, and shall detail any issues with the site or equipment, field calibration procedure, and any notable conclusions or results. The World Bank and key client counterparts shall also be provided with access to the vendor's data repository or monitoring platform for real-time analysis.

The assignment shall be deemed completed once two years of concurrent data is delivered in compliance with the minimum data recovery rates specified. At this point the vendor shall decommission each site and remove the solar measurement equipment, unless alternative arrangements outside the scope of this assignment/contract are made and endorsed by the relevant client/host agency.



2 Station Summary

Work performed	Installation and commissioning of solar and meteorological measurement station including			
	security fence.			
Commissioning date	14 December 2019			
Planned decommissioning date	14 December 2021			
Client	World Bank			
Client contact person and contact details	Name: Abdul Rahim Jalloh			
•	Email: Abduljay@gmail.com			
	Telephone: + 1 301 825 1628			
	•			
	Name: Chiara Rogate			
	Email: crogate@worldbank.org			
	Telephone: +1 202 250 0568			
	Name: Samwel Kessy			
	Email: samwel.kessy@tanesco.co.tz			
	Telephone: +255 754 593 817			
Site location	13.5 km North East of Shinyanga,			
	approximately 990 km North West of Dar es			
	Salaam, Tanzania.			
	32°E 36°E 40°E			
	p°s			
	6°S			
	10°5			
_				
Access	From Shinyanga central, head North on the B6			
	for approximately 12.5 km. before you reach			
	the TANESCO substation, take a right.			
	Continue for another 800 m and the station will			
Coordinates	be on your left.			
Coordinates	03° 37' 35.71" S, 33° 30' 55.23" E			
Floreties	(-3.62658611111, 33.5153416667)			
Elevation	1179 m AMSL			
Time zone (local and data logger)	GMT +3 local time zone			
Name and contact details of on-site	Name: Emmanuel Kiyenze			
contact person(s)	Cell: +255 785 971 265			



3 Map of area

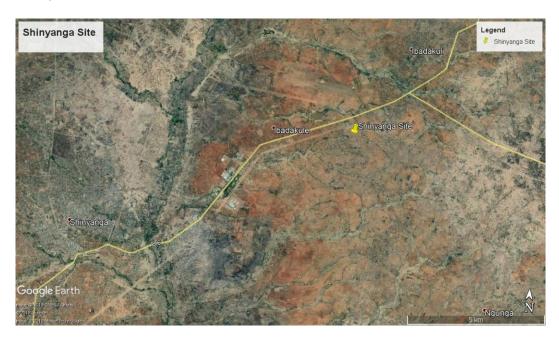


Figure 1: Map of the surrounding area (Source: Google Earth)

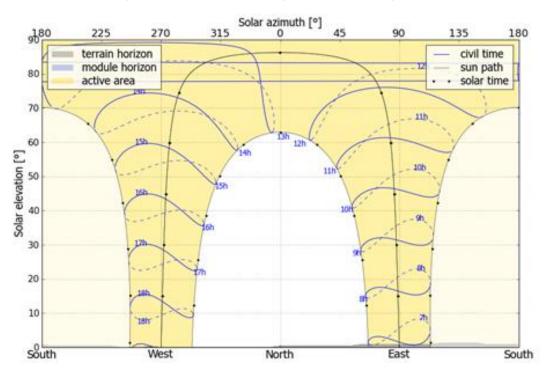


Figure 2: Terrain horizon and day length (Source: Solargis)



4 Site layout

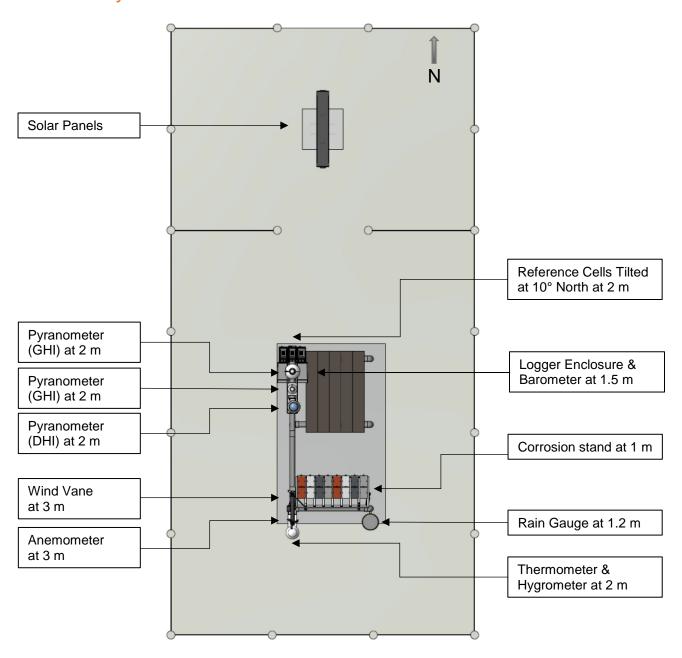


Figure 3: Site Layout (plan view)





Figure 4: Site Layout (perspective view)



5 Instrument list, serial numbers and multipliers

Instrument (Measurement)	Make and Model	Serial Number	Variable Name (Program)	Multiplier
Pyranometer (GHI)	Kipp & Zonen CMP 10	162969	GHI_1	8.51 µV/W/m²
Pyranometer (GHI)	Kipp & Zonen CMP 10	141003	GHI_2	9.58 μV/W/m²
Pyranometer (DHI)	Delta Electronics SPN 1	A1702	DHI_SPN1	1
Reference Cell (Clean)	Ingenieurbüro Si-mV-85-A	85-00205-17- 19350089	RefCellClean	59.18 μV/W/m²
Reference Cell (Monthly)	Ingenieurbüro Si-mV-85-A	85-00205-17- 19350090	RefCellMonthly	57.87 μV/W/m²
Reference Cell (Dirty)	Ingenieurbüro Si-mV-85-A	85-00205-17- 19350091	RefCellDirty	59.01 μV/W/m²
3-Cup Anemometer (Wind speed)	RM Young 03002	W002	WSpd	0.2 Offset 0.75 Slope
Wind Vane (Wind Direction)	RM Young 03002	W002	WDir	0 Offset 352 Slope
Temperature Sensor (Ambient Temperature)	Campbell Scientific CS215	E17297	Temp	1
Relative humidity Sensor (Relative Humidity)	Campbell Scientific CS215	E17297	RH	1
Barometer (Atmospheric Pressure)	Vaisala PTB110	K3520008	ВР	500 offset 0.24 slope
Rain Gauge (Rain)	HyQuest Solutions TB3/0.2mm	17-380	Rain	0.2 mm/tip
Corrosion Plate	Make	Sample	Position (Column, Row)	Mass (g)
		F3	C5, R1	127.2217
Mild Steel plate	Orytech Mild Steel	F4	C5, R2	165.4258
(Corrosion Testing)	Orytech Miliu Steel	F5	C6, R1	135.5167
		F6	C6, R2	132.8469
		F3	C3, R1	80.1289
Galvanised (Zinc) plate	Orytech H.D.	F4	C3, R2	80.0739
(Corrosion Testing)	Galvanised (Zinc)	F5	C4, R1	81.0270
		F6	C4, R2	79.8675
		F3	C1, R1	81.8963
Copper plate	Orytech Copper	F4	C1, R2	82.6888
(Corrosion Testing)	3966	F5	C2, R1	82.4204
		F6	C2, R2	81.4436
		F3	C7, R1	37.6331
Aluminium plate	Orytech Aluminium	F4	C7, R2	37.3479
(Corrosion Testing)	,	F5	C8, R1	37.2823
		F6	C8, R2	36.4383



6 Supporting hardware and communication peripherals

Data Logger	Campbell CR1000X (OS: Std.03.02)
Communication	RS232 (115200) TCP/IP
Pakbus Address	776
Password Set	None
Modem and Antenna	Maestro M100 3G modem with Poynting antenna
Network Details	Service provider: Airtel, Tanzania Phone number: 255 694 04 2934
Modem Power Control	SW12V
Data Logger Clock	GMT+3
Main Battery	2 x 12 V / 24 Ah
Solar Panel(s)	2 x 25 W
Charge Controller	2 x CPL Research (10 A)



7 Data logger wiring

Shinyanga Wiring Diagram November 2019 - CR1000X

Logger Port	Accessories	Connection	Instrument Cable	Function	Reading	Instrument
		1H	White / Red	Signal +		
		1L	Green / Blue	Signal -		
		AGB	Black	GND		
	SW12-2		Yellow	Heater +	GHI1	SR20 / CMI
		GB		Heater -		
VX1	10kΩ 0.1% Resistor	SE3	Red	Temp+		
		AG2	Blue	Temp -		
		3H	White / Red	Signal +		
		3L	Green / Blue	Signal -		
		AGB	Black	GND		
	SW12-2		Yellow	Heater +	GHI2	SR20 / CM
		GB		Heater -		
VX1	10kΩ 0.1% Resistor	SE4	Red	Temp +		
		AG2	Blue	Temp -		
		5H	White	GHI+		SDM
		6H	Brown	DHI+]	
		5L	Green	Signal -		
		- 6L				
		GB	Grey	0 V	D	
		PB	Pink	12 V	DHI	SPN1
	SW12-2		Red	Heater +		
		GB	Blue	Heater -	1	
		AGB	Clear	GND	1	
		NC	Yellow	Sun		
		РВ	Red	12 V		
		C1	Green	Signal +		
		GB	White	0 V	Temp & RH	CS215
		GB	Black	0 V		
		AGB	Clear	GND		
		SE13	Red	Signal +		
		AG6	Blue	Signal -	Clean	Ref cell
		AGB	Black	GND	1	
		SE14	Red	Signal +		
		AG7	Blue	Signal -	Monthly	Ref cell
		AGB	Black	GND	1 '	



Solar & Meteorological Station – Installation Report

		SE15	Red	Signal +		
		AG7	Blue	Signal -	Dirty	Ref cell
		AGB	Black	GND	-	
		VX2	Black	Excitation		
		SE16	Red	Signal +	WD	024A
		AG8	White	Signal -	VVD	U24A
		AGB	Clear	GND		
		P1	Black	Signal +		
		AG8	White	Signal -	WS	014A
		AGB	Clear	GND		
		P2	Black	Signal +		
		AG	White	Signal -	Rain	TE525
		AGB	Clear	GND		
5V	10kΩ Resistor	C8	Red	Signal +		
		C5	Green	Light +	Clean	Clean
		C3	Blue	Signal -	Clean	Button
		AGB	Clear	GND		
5V	10kΩ Resistor	C4	Yellow	Signal +		
		C5	Green	Light +	Monthly	Monthly
		C3	Blue	Signal -	Widiting	Button
		AGB	Clear	GND		
5V	10kΩ Resistor	C6	Red	Signal +		
		G	Blue	Signal -	Gate	Switch
		AGB	Clear	GND		
		SE4	Blue/Brown	Signal +		
		12V	Red	12V		
		C7	Green	Signal +	Draceura	DTD110
		AG4	Black	Signal -	Pressure	PTB110
		AG4	Yellow/White	GND		
		AGB	Clear	GND		



8 Power circuit diagram

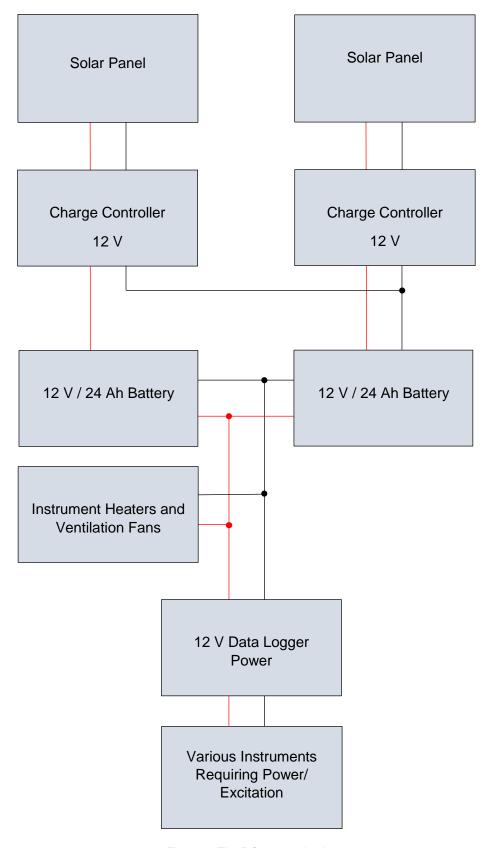


Figure 5: The DC power circuit



9 Detail Photographs

This section showcases details of the installation, including the main station components. Records are shown of instrument makes, models and serial numbers, as well as the installation levels and orientation where applicable.



Figure 6: Station Summary





Figure 7: GHI (1) Pyranometer Installation



Figure 8: GHI (2) Pyranometer Installation





Figure 9: DHI Pyranometer Installation



Figure 10: Wind instruments at 3 m





Figure 11: Thermometer and Hygrometer at 2 m



Figure 12: Corrosion Test Stand





Figure 13: Rain Gauge

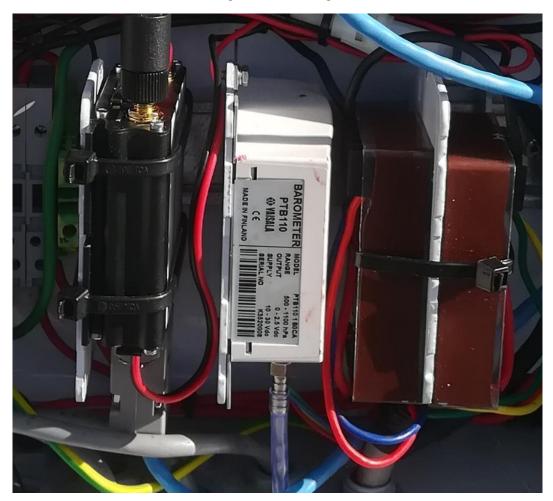


Figure 14: Barometer





Figure 15: Reference Cells at 10° North





Figure 16: Solar Panel



Figure 17: Logger Enclosure



10 Terrain Photographs

Obstacles protruding higher than the horizon as viewed from the solar instruments will affect lower solar elevation readings if they fall within the sun path as depicted in Figure 2. The pictures in this section shows the terrain surrounding the station at the time of installation, giving an indication of near or far shading influences on the station.



Figure 18: 0/360 Degrees (North)





Figure 19: 30 Degrees



Figure 20: 60 Degrees





Figure 21: 90 Degrees (East)



Figure 22: 120 Degrees





Figure 23: 150 Degrees



Figure 24: 180 Degrees (South)





Figure 25: 210 Degrees



Figure 26: 240 Degrees





Figure 27: 270 Degrees (West)



Figure 28: 300 Degrees





Figure 29: 330 Degrees



11 Station Photographs

This section indicates the station within the surrounding terrain to give an overall view thereof, as well as provide additional context to the possible near and far shading influences.



Figure 30: 0/360 Degrees (From North)





Figure 31: 30 Degrees



Figure 32: 60 Degrees





Figure 33: 90 Degrees (From East)



Figure 34: 120 Degrees





Figure 35: 150 Degrees



Figure 36: 180 Degrees (From South)





Figure 37: 210 Degrees



Figure 38: 240 Degrees





Figure 39: 270 Degrees (From West)



Figure 40: 300 Degrees





Figure 41: 330 Degrees



12 Calibration Certificates

Calibration Certificate



Pyranometer ISO 9847 Calibration

Calibrated Instrument

Instrument: Pyranometer Manufacturer: Kipp & Zonen

Model: CMP10

ISO 9060:1990 Class: Secondary Standard

Calibration Date: 05 November 2019

Serial Number: 162969 New Sensitivity: 8.51 µV/W/m²


Certificate Number: GSACA-0884

Calibration Methodology

GeoSUN performed an indoor calibration through exposure of both the calibrated instrument (instrument under test) and a reference instrument to an artificial light as radiation source and comparing the sensor outputs. The instruments were installed on a common horizontal base and regularly checked to ensure that it remained clean and level for the duration of the reference data being collected. The calibration was performed in accordance with the ISO 9847 (1992) standard, procedure type IIc.

Reference Instrument and its Traceability

The reference instrument is a Kipp & Zonen CMP21 pyranometer (SN 150545). The instrument was calibrated on 17 April 2019 at ISO-CAL North America against absolute cavity radiometer AHF-28560 which successfully participated at IPC-XII with the World Standard Group of radiometers. The location of ISO-CAL is at 20th street, Phoenix, Arizona in the USA at latitude 33.8176944°, longitude -112.0396083° and altitude 570 m AMSL. The reference instrument was calibrated at normal incidence with the sun and sky radiation as the source using the "alternating sun-and-shade method". The readings are referenced to the World Radiometric Reference (WRR) as stated in the WMO Technical Regulations, originally with an SI relative uncertainty estimated at ±0.3%. The diagram on the right shows the traceability hierarchy.



Absolute Uncertainty

The absolute uncertainty is the combined result of three uncertainties namely:

1) The expanded uncertainty during calibration of the reference instrument, given as ±0.47%.

2) The uncertainty in the correction of directional errors (cosine errors), estimated by scientific judgement as ±0.5%.

3) The expanded uncertainty of the transfer procedure (calibration by comparison), estimated by scientific judgement as ±1%. The combined expanded uncertainty is the root sum of the squares, resulting in $\sqrt{(0.472 + 0.52 + 12)} = \pm 1.21\%$.

Calibration Environment, Results and Instrument Status

The calibration was performed at latitude -33.96543°, longitude 18.83626° and altitude 134 m AMSL and was concluded on 05 November 2019 at 15:46. A calibration was done using the measured output of the test instrument, of which the calibration environment and results are stated below. The measurement results recorded in this certificate were correct at the time of calibration. The subsequent accuracy will depend on factors such as care, handling and frequency of use. The calibration certificate or report may not be reproduced except in full, without the written approval of the laboratory. Considering the operating conditions and the IEC 61724-1:2017 standard requirements, GeoSUN recommends an annual calibration.

Instrument Status Bubble Level: Good

Dome: Abrasions present, Replaced

Calibration Environment - Average [Range]

Irradiation: 442 [441 - 444] W/m² Ambient Temperature: 24.3 [24.0 - 24.7] °C Reference Instrument Temp.: 24.4 [24.2 - 24.7] °C

Original Calibration

Original Sensitivity: 8.74 µV/W/m² Original Calib. Date: 23 November 2018 Calibration Results

New Sensitivity: 8.50748 μ V/W/m² Sensitivity Standard Deviation (σ_{n-1}): 0.00321 μ V/W/m²

Calibration Uncertainty (k = 2): ±0.1032 µV/W/m2 (±1.21%)

Data Quantity: 4 Series, 16 Samples Next Calibration: November 2020

Calibrated by: W.C. Engelbrecht Magallude

Authorised by:

Mdefaga M.L. de Jager



GeoSUN Africa (Pty) Ltd Unit 1, CS Africa Building, 1 Meson Street, Techno Park, Stellenbosch, South Africa info@geosun.co.za, www.geosun.co.za,+27 21 882 8354

Page 1 of 1 End of certificate



Calibration Certificate



Pyranometer ISO 9847 Calibration

Calibrated Instrument

Instrument: Pyranometer Manufacturer: Kipp & Zonen

Model: CMP10

ISO 9060:1990 Class: Secondary Standard

Calibration Date: 06 August 2019

Serial Number: 141003

Certificate Number: GSACA-0818


New Sensitivity: 9.58 µV/W/m2

Calibration Methodology

GeoSUN performed an indoor calibration through exposure of both the calibrated instrument (instrument under test) and a reference instrument to an artificial light as radiation source and comparing the sensor outputs. The instruments were installed on a common horizontal base and regularly checked to ensure that it remained clean and level for the duration of the reference data being collected. The calibration was performed in accordance with the ISO 9847 (1992) standard, procedure type IIc.

Reference Instrument and its Traceability

The reference instrument is a Kipp & Zonen CMP21 pyranometer (SN 110811). The instrument was calibrated on 14 August 2018 at ISO-CAL North America against absolute cavity radiometer AHF-28560 which successfully participated at IPC-XII with the World Standard Group of radiometers. The location of ISO-CAL is at 20th street, Phoenix, Arizona in the USA at latitude 33.8176944°, longitude -112.0396083° and altitude 570 m AMSL. The reference instrument was calibrated at normal incidence with the sun and sky radiation as the source using the "alternating sun-and-shade method". The readings are referenced to the World Radiometric Reference (WRR) as stated in the WMO Technical Regulations, originally with an SI relative uncertainty estimated at ±0.3%. The diagram on the right shows the traceability hierarchy.



Absolute Uncertainty

The absolute uncertainty is the combined result of three uncertainties namely:

- The expanded uncertainty during calibration of the reference instrument, given as ±0.44%.
- 2) The uncertainty in the correction of directional errors (cosine errors), estimated by scientific judgement as ±0.5%.

3) The expanded uncertainty of the transfer procedure (calibration by comparison), estimated by scientific judgement as $\pm 1\%$. The combined expanded uncertainty is the root sum of the squares, resulting in $\sqrt{(0.44^2 + 0.5^2 + 1^2)} = \pm 1.20\%$.

Calibration Environment, Results and Instrument Status

The calibration was performed at latitude -33.965467°, longitude 18.836348° and altitude 134 m AMSL and was concluded on 06 August 2019 at 10:03. A calibration was done using the measured output of the test instrument, of which the calibration environment and results are stated below. The measurement results recorded in this certificate were correct at the time of calibration. The subsequent accuracy will depend on factors such as care, handling and frequency of use. The calibration certificate or report may not be reproduced except in full, without the written approval of the laboratory. Considering the operating conditions and the IEC 61724-1:2017 standard requirements, GeoSUN recommends an annual calibration.

Instrument Status Rubble Level: Good Dome: Good

Calibration Environment - Average [Range]

Irradiation: 574 [536 - 612] W/m² Ambient Temperature: 19.6 [19.2 - 19.9] °C Reference Instrument Temp.: 20.0 [19.6 - 20.4] °C

Original Calibration

Original Sensitivity: 9.67 µV/W/m² Original Calib. Date: 05 November 2014 Calibration Results

New Sensitivity: 9.58238 µV/W/m² Sensitivity Standard Deviation (σ_{n-1}): 0.00064 μV/W/m²

Calibration Uncertainty (k = 2): $\pm 0.1151 \,\mu\text{V/W/m}^2$ ($\pm 1.20\%$)

Data Quantity: 4 Series, 16 Samples Next Calibration: August 2020


Cambrated by:
W.C. Engelbrecht
Mngallads

Authorised by: M.L. de Jager

Page 1 of 1







Calibration Certificate

This is to certify that the Sunshine Pyranometer type SPN1 identified below has been calibrated in accordance with Delta-T Devices Ltd standard production procedures and conforms to the specifications as detailed.

Serial Number	SPN1 - A1702
Date	10/05/19
Authorised Signature	4

We recommend that this instrument is recalibrated every 2 years.

Traceability

The SPN1 is calibrated under a uniform light source which simulates the solar spectrum, against a transfer standard SPN1. The transfer standard is calibrated outdoors against a Kipp & Zonen CM21 secondary standard pyranometer (calibration traceable to the World Radiometric Reference), with solar tracker and shading disk for diffuse measurement.

Accuracy, Total (Global) and Diffuse radiation

When correctly calibrated, the expected accuracy is given in the table below. The figures give 95% confidence limits, i.e. 95% of individual readings will be within the stated limits under normal climatic conditions.

Overall accuracy;	±5% daily integrals ±5% ±10 W.m ² hourly averages ±8% ±10 W.m ² individual readings	
Range	0 to >2000 W.m ⁻²	
Analogue output sensitivity	1mV = 1 W.m ⁻²	



Delta-T Devices Ltd

130 Low Road, Burwell, Cambridge, CB25 0EJ, UK
Tel: +44 1638 742922 Fax: +44 1638 743155
email: sales@delta-t.co.uk web: www.delta-t.co.uk





INGENIEURBÜRO Calibration Certificate Silicon Irradiance Sensor Mencke & Tegtmeyer GmbH Meßgeräte für die Solartechnik Sensor Type: Si-mV-85-A Schwarzer Weg 43A Serial No.: 85-00205-17-19350089 31789 Hameln, Germany Comment: www.ib-mut.de Irradiance Calibration with Artificial Light in Comparison to a Reference Cell Calibrated by: Huhnstock-Breuer Date / Time: 28.08.2019 Type Calibration Temperature Coefficient Output Temperature Irradiance¹⁾ µV/W/m² 1/°C Reference Cell Si-Ref mono PTB-1 56.51 0,00067 56,953 30,76 1004,0 Irradiance Correction Factor 31 Output Temperature Calibration µV/W/m² mV Test Object Si-mV-85-A 1004,0 0.995880 59,659 30,91 59,18 Test Equipment Irradiance Calibration Type Si-Ref mono Serial No. Calibration Certificate 02-20002-05- 47109-PTB-18 Manufacturer Ingenieurbüro Mencke & Tegtmeyer GmbH PTB PTB-1 15309999 098220-02 D-K-15019-01-00 098221-02 D-K-15019-01-00 Gantner Instruments IDL100 191667 DKD ISM111 078743 DKD OMEGA Engineering IN510 9894 Output * 1000 ${}^{11}Irradiance = \frac{1}{Calibration*(1 + Temperature\ Coefficient*(Temperature\ -25))}$ 2) Calibration = Output * 1000 * Correction Factor Irradiance ³¹Individual calculated for each Calibration Process, must not be used for Outdoor Application.





INGENIEURBÜRO Calibration Certificate Silicon Irradiance Sensor Mencke & Tegtmeyer GmbH Meßgeräte für die Solartochnik Sensor Type: Si-mV-85-A Schwarzer Weg 43A Serial No.: 85-00205-17-19350090 31789 Hameln, Germany Comment: www.ib-mut.de Irradiance Calibration with Artificial Light in Comparison to a Reference Cell Calibrated by: Huhnstock-Breuer Date / Time: 28.08.2019 13:49 Туре Calibration Temperature Coefficient Output Temperature Irradiance¹⁾ µV/W/m² 1/°C mV W/m² Reference Cell Si-Ref mono PTB-1 56,51 0.00067 56.953 30.76 1004,0 Correction Factor 3) Type Irradiance Output Temperature Calibration W/m² µV/W/m² Test Object Si-mV-85-A 1004,0 0.996130 58,326 Test Equipment Irradiance Calibration Serial No. Calibration Certificate 02-20002-05- 47109-PTB- 8 15309999 Manufacturer Type Si-Ref mono Ingenieurbüro Mencke & Tegtmeyer GmbH PTB PTB-1 098220-02 D-K-15019-01-00 098221-02 D-K-15019-01-00 Gentner Instruments IDL100 191007 ISM111 078743 DKD OMEGA Engineering IN510 9894 Output + 1000 ${}^{(1)}Irradiance = \frac{1}{Calibration*(1 + Temperature\ Coefficient*(Temperature\ -25))}$ ²⁾Calibration = Output * 1000 * Correction Factor Irradiance ³¹ Individual calculated for each Calibration Process, must not be used for Outdoor Application.





INGENIEURBÜRO Calibration Certificate Silicon Irradiance Sensor Sensor Type: Si-mV-85-A Schwarzer Weg 43A Serial No.: 85-00205-17-19350091 31789 Hameln, Germany Comment: www.ib-mut.de Irradiance Calibration with Artificial Light in Comparison to a Reference Cell Calibrated by: Huhnstock-Breuer Date / Time: 28.08.2019 13:49 Calibration Temperature Coefficient Output Temperature Irradiance¹⁾ mV W/m² Si-Ref mono PTB-1 Reference Cell 56,51 0,00067 56,953 30.76 1004.0 Correction Factor 2) Type Irradiance Output Temperature Calibration W/m² µV/W/m² Test Object Si-mV-85-A 1004.0 0.996130 59,470 30,55 **Test Equipment Irradiance Calibration** Serial No. Calibration Certificate 02-20002-05- 47109-PTB-18 Ingenieurbüro Mencke & Tegtmeyer GmbH PTB-1 15309999 Gäntner Instruments IDL100 191667 098220-02 D-K-15019-01-00 DKD ISM111 078743 098221-02 D-K-15019-01-00 DKD OMEGA Engineering IN510 9894 Output * 1000 *) $trradiance = \frac{1}{Calibration * (1 + Temperature Coefficient * (Temperature - 25))}$ $^{2)}Calibration = \frac{Output * 1000 * Correction Factor}{t}$ Irradiance ³¹ Individual calculated for each Calibration Process, must not be used for Outdoor Application.



Calibration Certificate



ISO 9001 Meteorological Calibration

Station Name: Shinyanga Meteorological Station Location: -33.965447°, 18.8361658° Calibration Date: 21 November 2019 Ambient conditions: 25 - 27 °C; 50 - 52 % RH

Test	Paramete		Reference	Test	Uncert	ainty (±)*
Instrument	Paramete	er	Reading	Reading	Instr.	Absolute
Campbell Scientific Model CS215	Ambient Temperature		3,3 ℃	3.7 °C	0.9 °C	1.9 °C
SN E17292			42.3 °C	43.0 °C	0.5 C	1.5 C
Campbell Scientific Model CS215	Relative Humidity	At 24°C →	16.3 % RH	18.7 %RH	2 % RH	5.6 % RH
SN E17292		At 24°C →	72.8 % RH	74.3 % RH	2 70 KH	3.0 70 KH
Vaisala PTB110	Barometric Pressure		700.8 hPa	701.8 hPa		
SN K3520008			800.7 hPa	798.6 hPa	1.5 hPa	2.7 hPa
			998.3 hPa	998.3 hPa	1.5 nPa	Z./ nPa
			1097.9 hPa	1100.4 hPa		
RM Young 03002-5	Wind Speed	200 rpm →	2.7 m/s	2.7 m/s		
GSASN-W002		400 rpm →	5.2 m/s	5.2 m/s		
	$m/s = (rpm \times 0.0125) + 0.2$	800 rpm →	10.2 m/s	10.2 m/s	1 m/s	1.0 m/s
		1 800 rpm →	22.7 m/s	22.7 m/s	1 mys	1.0 m/s
		2 400 rpm →	30.2 m/s	30.2 m/s		
		3 000 rpm →	37.7 m/s	37.7 m/s		
RM Young 03002-5	Wind direction		North	0°		
GSASN-W002			East	90°	5 °	10 °
			South	180 °	,	10
			West	270 °		
Hyquest Solutions TB3/0.2mm	Precipitation Tip	s =	250 ml		7.5 ml	11.5 ml
SN 17-380	1190	6.28 ml/Tip	39 Tips	40 Tips	1 Tip	2 Tips

Comments: The rain gauge sensitivity was adjusted.

Reference Ins	truments						
Parameter	Reference Instrument Serial Number Traceability Calibration Date			ertain Expand			
Temperature Relative Humidity	Campbell Scientific 109 Rotronic HC2A-SH	15553-29 20261232	South African National Standard (NMISA) Swiss National Standard (Rotronic)	05-Sep-19 03-Sep-19	0.01 1.1	1.02 3.6	°C % RH
Barometric Pressure Precipitation	Vaisala PTB110 Glassco Measuring Cyl.	L2850725 05.15/2028	South African National Standard (Inteltronics) Indian National Standard (Glassco)	09-Sep-19 19-Sep-19	0.2	1.2 4.02	hPa ml
Wind Speed	Young 18802 Drive	4664	South African National Standard (LabCom)	28-Aug-19	2	3	rpm

* Expanded uncertainty includes the reference's accuracy and calibration uncertainty, and this calibration's transfer uncertainty. Absolute calibration uncertainty includes the test instrument accuracy. Although the test instrument increment resolution can have an effect on the uncertainty, it is not taken into account.

Calibration Methodology

Reference and test instruments were sealed and submerged in warm and cold water sources for respective measurements. Temperature:

Relative Humidity: Reference and test instruments were tested in a low humidity chamber and at ambient conditions.

Barometric Pressure: Reference and test instruments were connected to a closed pressure system and different pressures were induced. Precipitation: A set volume of water was poured through the rain gauge at an acceptable flow rate and the amount of tips were counted.

Wind Speed: A drive was coupled to the anemometer shaft, set rotational speeds were applied and wind speed recorded. The wind vane was handheld at roughly 90° increment angles while angle outputs were recorded.

Calibrated by:

W.C. Engelbrecht Wingslesso

Approved by: M.L. de Jager Malaga



Unit 1, CS Africa Building, 1 Meson Street, Techno Park, Stellenbosch, South Africa info@geosun.co.za, www.geosun.co.za,+27 21 882 8354

2018/06/16
